


Project Delivery - Advertisement, All Programs, VTrans/Operations

Key Activity:
 Program:
 Contract Responsibility:
 Snapshot:

Goal: 80% within 30 days

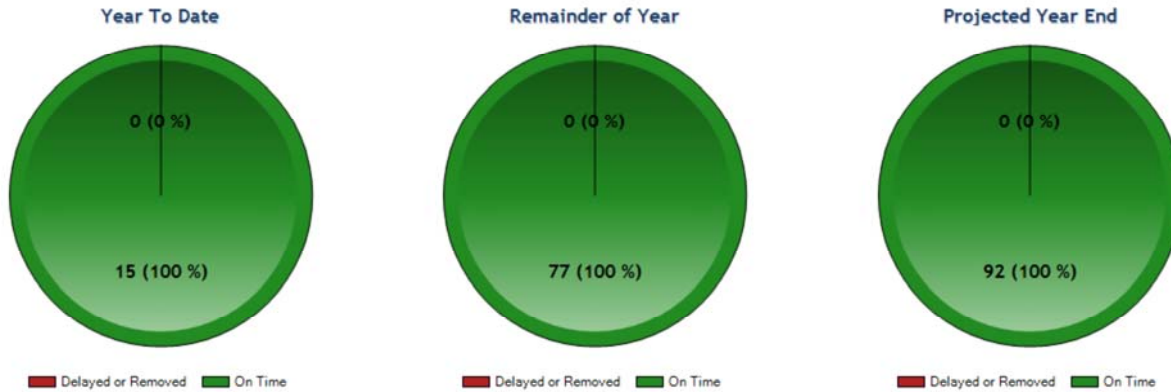

Advertisement for All Programs (VTrans/Operations)

Program	Year To Date			Remainder of Year			Projected Year End		
	On-Time	Delayed or Removed	% On-Time	On-Time	Delayed or Removed	% On-Time	On-Time	Delayed or Removed	% On-Time
Bike & Pedestrian Facilities	0	0	0	2	0	100	2	0	100
Interstate Bridges	0	0	0	1	0	100	1	0	100
Maintenance	0	0	0	2	0	100	2	0	100
Paving	2	0	100	17	0	100	19	0	100
Rail	1	0	100	12	0	100	13	0	100
Roadway Projects	2	0	100	13	0	100	15	0	100
Safety & Traffic Operations	1	0	100	15	0	100	16	0	100
State Highway Bridges	4	0	100	8	0	100	12	0	100
Town Highway Bridges	5	0	100	7	0	100	12	0	100
All Programs:	15	0	100 %	77	0	100 %	92	0	100 %

Advertisement, Remainder of Year On-Time Projects for Paving (VTrans/Operations)

PIN	Project	Snapshot Expected Start	Snapshot Actual Start	Today's Expected Start	Today's Actual Start
07C214	LEMINGTON-CANAAN STP 2723(1)	5/27/2015		5/27/2015	
14V200	MANCHESTER-RUTLAND TOWN NH SURF(50)	12/30/2015		12/30/2015	
11D340	SOUTH BURLINGTON-WILLISTON NH 2944(1)	6/3/2015		6/3/2015	
99C194	THETFORD STP 2221(1)S	8/5/2015		8/5/2015	
09C362	WESTFIELD-TROY STP 2903(1)	6/10/2015		6/10/2015	
12D224	WILLISTON NH 2949(1)	6/3/2015		6/3/2015	
14V231	WORCESTER-ELMORE STP 2954(1)	8/26/2015		8/26/2015	
<u>12</u>					
