


Lamoille Valley Rail Trail (LVRT) – Construction Update

HOUSE TRANSPORTATION COMMITTEE, FEB. 10, 2021

JOEL PERRIGO, INTERIM MUNICIPAL ASSISTANCE PROGRAM MANAGER,
VERMONT AGENCY OF TRANSPORTATION

Lamoille Valley Rail Trail St. Johnsbury to Swanton, VT 2020-2022 Trail Work Areas

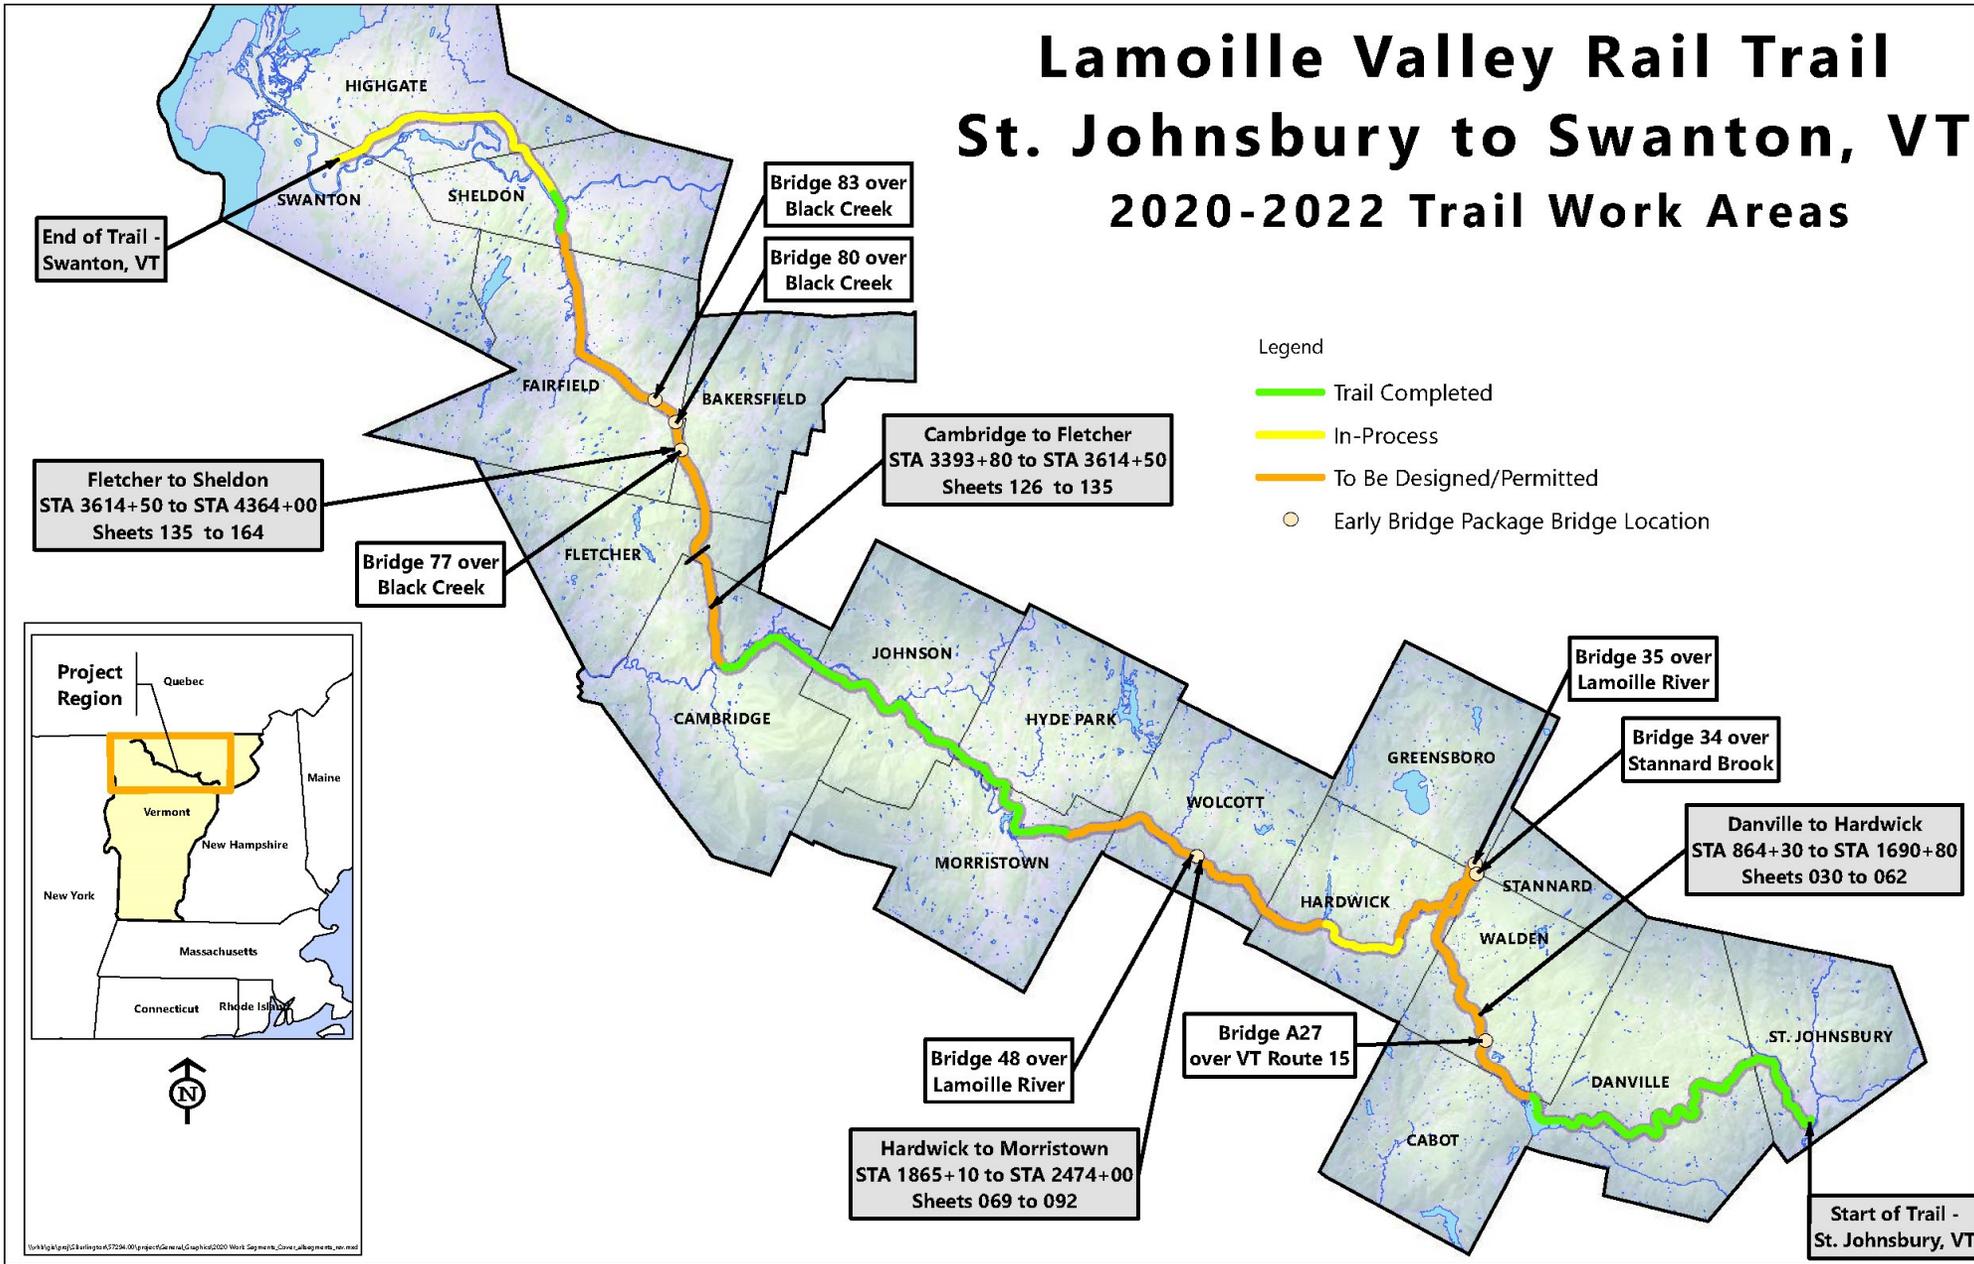

CURRENT PROJECTS

- July 2020 – Funding approved for the build out
- Two projects were identified as shelf ready:
 - Swanton to Highgate, 3.88 miles
 - IDIQ
 - Awarded, Constructed, Complete
 - Highgate to Sheldon, 6.29 miles
 - Standard Design Bid Build
 - Awarded, under Construction
 - Currently winter shutdown
 - To be completed June 2021

CHALLENGES







UPCOMING

- Early bridge project scheduled for March 2021 advertisement, Construction Summer 2021
 - Replacement of 6 bridges with prefabricated pedestrian trusses
- 3 trail segments, all beginning Summer 2021, to be completed by June 2022
 - Fletcher to Sheldon
 - Hardwick to Morristown
 - Danville to Hardwick



Joel Perrigo

joel.perrigo@vermont.gov

802.595.4933
